GANTT CHART
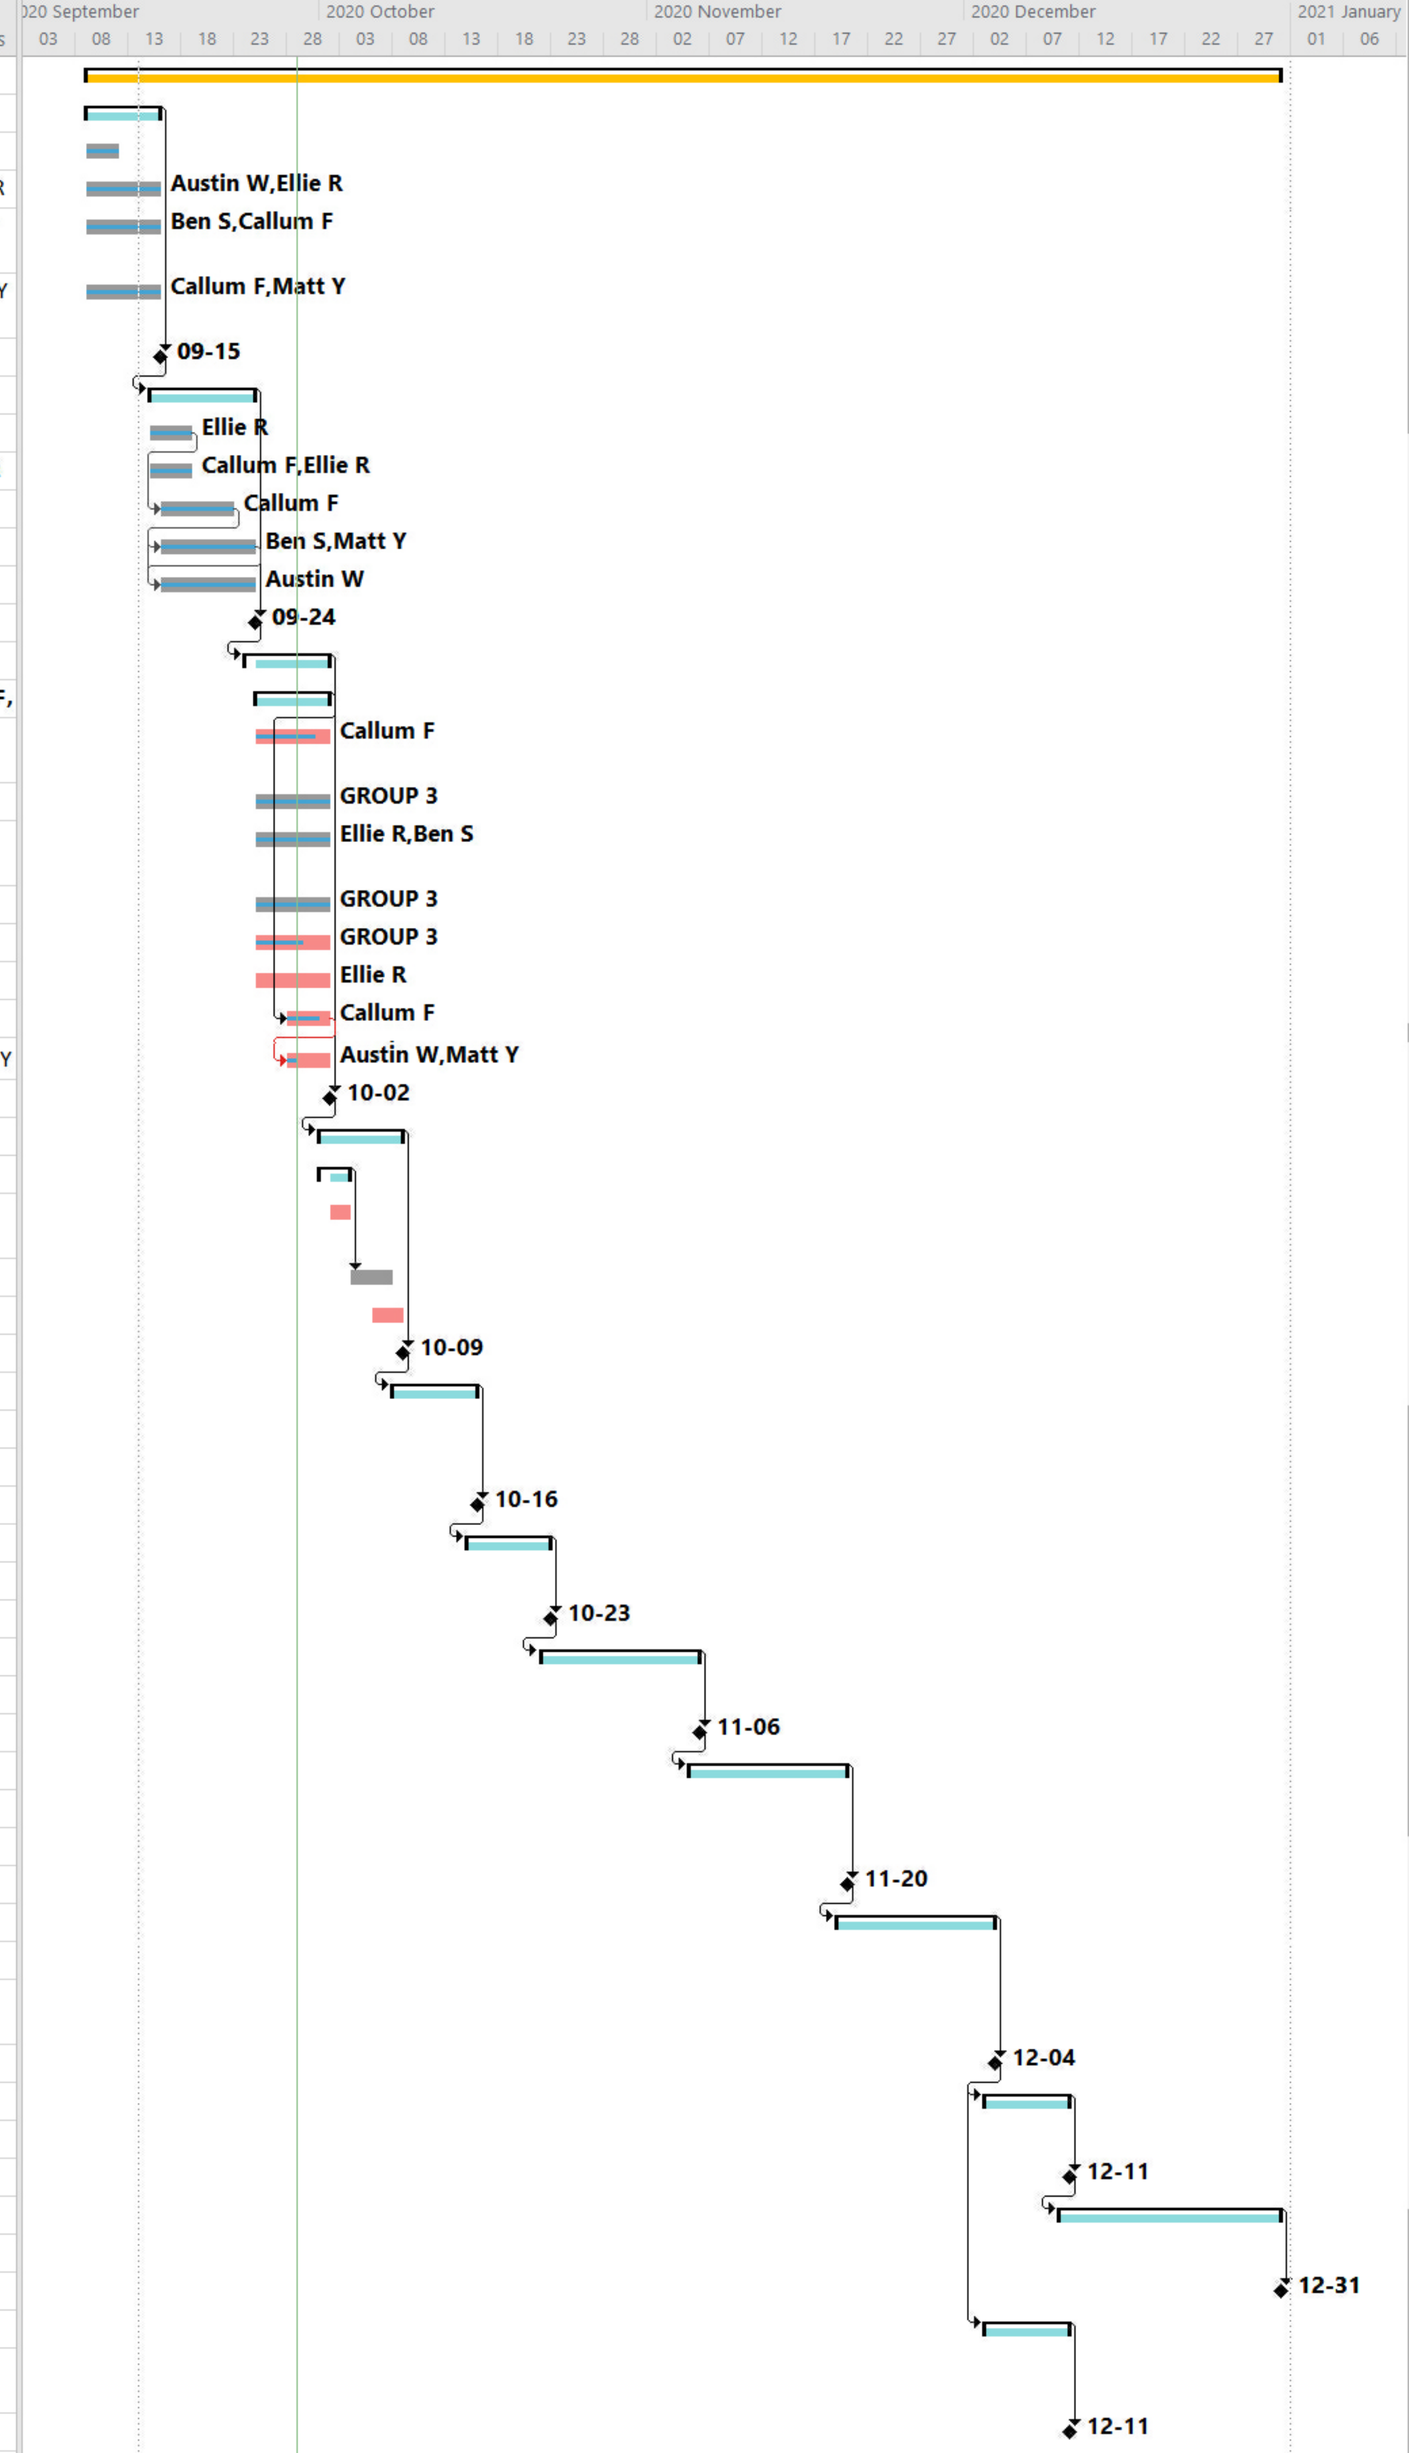
	Task Name	Duration	Start	Finish	Predecessors	Resource Names
1	**Accessible Digital Drawings**	**81 days?**	**Wed 20-09-09**	**Wed 20-12-30**		**GROUP 3**
2	**Project Deliverables A**	**5 days**	**Wed 20-09-09**	**Tue 20-09-15**		
3	First Group Meeting	3 days	Wed 20-09-09	Fri 20-09-11		
4	Team Contract	5 days	Wed 20-09-09	Tue 20-09-15		Austin W,Ellie R
5	Client Meeting Preperation	5 days	Wed 20-09-09	Tue 20-09-15		Ben S,Callum F
6	Project Management Skeleton	5 days	Wed 20-09-09	Tue 20-09-15		Callum F,Matt Y
7	SUBMIT Deliverable A	0 days	Tue 20-09-15	Tue 20-09-15	2	Callum F
8	**Project Deliverables B**	**8 days?**	**Tue 20-09-15**	**Thu 20-09-24**	**7**	
9	Need Statements	4 days	Tue 20-09-15	Fri 20-09-18		Ellie R
10	Project Statements	4 days	Tue 20-09-15	Fri 20-09-18		Callum F,Ellie R
11	Metrics	5 days	Wed 20-09-16	Tue 20-09-22	9	Callum F
12	Benchmarking	7 days	Wed 20-09-16	Thu 20-09-24	11	Ben S,Matt Y
13	Target Specifics	7 days	Wed 20-09-16	Thu 20-09-24	11,12	Austin W
14	SUBMIT Deliverable B	0 days	Thu 20-09-24	Thu 20-09-24	8	Ellie R
15	**Project Deliverable C**	**6 days?**	**Thu 20-09-24**	**Thu 20-10-01**	**14**	
16	**Conceptual Design**	**5 days**	**Fri 20-09-25**	**Thu 20-10-01**		**Ben S,Callum F,**
17	Functional Decomposition	5 days	Fri 20-09-25	Thu 20-10-01		Callum F
18	Product Concepts	5 days	Fri 20-09-25	Thu 20-10-01		GROUP 3
19	Analysis and Evaluation	5 days	Fri 20-09-25	Thu 20-10-01		Ellie R,Ben S
20	Promising Solutions	5 days	Fri 20-09-25	Thu 20-10-01		GROUP 3
21	Group Design	5 days	Fri 20-09-25	Thu 20-10-01		GROUP 3
22	Visual Representation	5 days	Fri 20-09-25	Thu 20-10-01		Ellie R
23	Project Plan	4 days	Mon 20-09-28	Thu 20-10-01	16	Callum F
24	Feasibility Study	4 days	Mon 20-09-28	Thu 20-10-01	23	Austin W,Matt Y
25	SUBMIT Deliverable C	0 days	Fri 20-10-02	Fri 20-10-02	15	Callum F
26	**Project Deliverable D**	**6 days?**	**Thu 20-10-01**	**Thu 20-10-08**	**25**	
27	**Detailed Design**	**3 days**	**Thu 20-10-01**	**Sat 20-10-03**		
28	Prototype Feature and Task Breakdown	2 days	Fri 20-10-02	Sat 20-10-03		
29	Prototype 1	4 days	Sun 20-10-04	Wed 20-10-07	27	
30	BOM	3 days	Tue 20-10-06	Thu 20-10-08		
31	SUBMIT Deliverable D	0 days	Fri 20-10-09	Fri 20-10-09	26	Callum F
32	**Project Deliverable E**	**6 days?**	**Thu 20-10-08**	**Thu 20-10-15**	**31**	
33	Project Process					
34	Presentation					
35	SUBMIT Deliverable E	0 days	Fri 20-10-16	Fri 20-10-16	32	Callum F
36	**Project Deliverable F**	**6 days?**	**Thu 20-10-15**	**Thu 20-10-22**	**35**	
37	Buisness Model					
38	SUBMIT Deliverable F	0 days	Fri 20-10-23	Fri 20-10-23	36	Callum F
39	**Project Deliverable G**	**11 days?**	**Thu 20-10-22**	**Thu 20-11-05**	**38**	
40	Prototype 2					
41	SUBMIT Deliverable G	0 days	Fri 20-11-06	Fri 20-11-06	39	Callum F
42	**Project Deliverable H**	**11 days?**	**Thu 20-11-05**	**Thu 20-11-19**	**41**	
43	Economic Report					
44	1 Minute Pitch Video					
45	SUBMIT Deliverable H	0 days	Fri 20-11-20	Fri 20-11-20	42	Callum F
46	**Project Deliverable I**	**11 days?**	**Thu 20-11-19**	**Thu 20-12-03**	**45**	
47	Design Day Pitch					
48	Final Prototype Evaluation					
49	SUBMIT Deliverable I	0 days	Fri 20-12-04	Fri 20-12-04	46	Callum F
50	**Project Deliverable J**	**6 days?**	**Thu 20-12-03**	**Thu 20-12-10**	**49**	
51	User Manual					
52	SUBMIT Deliverable J	0 days	Fri 20-12-11	Fri 20-12-11	50	Callum F
53	**Project Deliverable K**	**15 days?**	**Thu 20-12-10**	**Wed 20-12-30**	**52**	
54	Final Presentation					
55	SUBMIT Deliverable K	0 days	Thu 20-12-31	Thu 20-12-31	53	Callum F
56	**Project Deliverable L**	**6 days?**	**Thu 20-12-03**	**Thu 20-12-10**	**49**	
57	Intelectual Property Search					
58	SUBMIT Deliverable L	0 days	Fri 20-12-11	Fri 20-12-11	56	Callum F
